


Site Odour Check List Site name: Wanlip Time and Date: 02/10/2024 Print Initials: DW Circle: Reactive or Proactive (Record customer details in act	ions/next steps for Reactive complaints)
1. Wind direction	8. Weather conditions
Specify 14.1 ENE	Specify - Overcast - Wet
2. Flows into works/ FFT 3600 L/S	
High (2800-3600 L/s) Medium (1300-2800 l/s) Low (0-1300 l,	9. Odour present at inlet cha
Actual flow - 3626 L/S	High Medium
3. Odour present at on site SPS?	
Yes No	
4. Screenings and grit removed from site as per contact	Actions/Next Steps/ OOS Assets/ Any a
agreement (Inlet, PFT and CDE)?	information regarding site issues etc.
N.	Biffa: Garage doors open 2 N/W PST 4 OOS
Yes No	O/W Lane 1 Aerator 5 OOS
5. Out of service PST's drained and cleaned?	O/W Lane 2 Aerator 1 OOS
5. Out of service 151 5 dramed and decaned.	O/W Lane 2 Aerator 4 OOS
Yes No	O/W Lane 8 Aerator 5 OOS
	O/W Lane 11 Aerator 1 OOS
6. Out of service PFT's drained and cleaned?	O/W Lane 13 Aerator 2 OOS O/W Lane 16 Aerator 5 OOS
	O/W FST 5 OOS
Ves) No	0/11/3/3/003

7. PFT and PST Red Golden Measure ALB's?

No

Yes

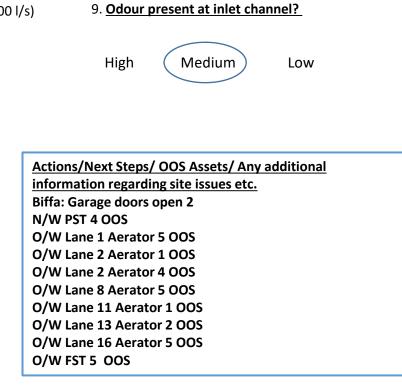

10. An	y odour	present at	plants	operated	by other
busine	sses (e.g	g. Biffa)?	-	-	-



11. Is on site odour control working?



13. Any other operational issue potentially effecting odour?

YES	NO	

13. Any other known area odours?

		_
YES	NO	
ILJ	NO	

Key:

- CDE screens = imported sludge screens
- PST = primary settlement tanks
- PFT = Picket Fence Thickener
- SPS = sewage pumping station
- ALB = action limit breach
- L/S = Litres per second
- FFT = Full flow treatment before we divert to storm tanks
